
# D.H. WHITE ELEMENTARY MODULAR REPLACEMENT

#### **JANUARY 2023**

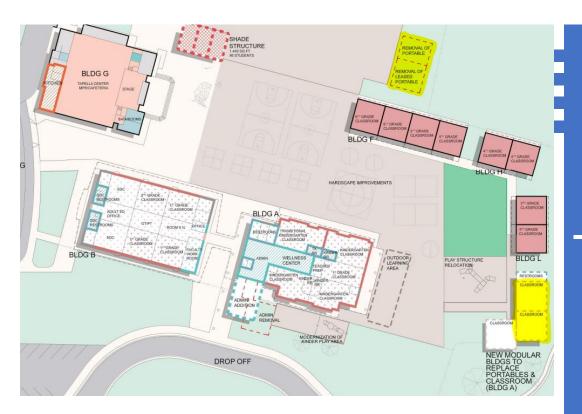

# **PROJECT DESCRIPTION**

The existing portables behind Building F will be removed as they are currently being leased by the District and are at the end of their useful life. They will be replaced with reconditioned modular buildings that will be installed on a permanent concrete foundation. The modular buildings will be placed near Building L as indicated in the master plan.

#### UPDATE:

- Division of the State Architect (DSA) approval
- Awarded to contractor November 2022.
- Construction to begin weather permitting

#### RIVER DELTA UNIFIED SCHOOL DISTRICT



## SCOPE

TWO (2) MODULAR BUILDINGS TO REPLACE EXISTING PORTABLES

## BUDGET

PROJECT BUDGET: \$860,169 FINAL BUDGET: \$853,342

# SCHEDULE

DESIGN: SUMMER 2022 STATE APPROVAL: SUMMER 2022 BID: FALL 2022 CONSTRUCTION: WINTER 2023 MOVE IN: FALL 2023

